ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
0		**CICS525_ProjectPlanV1.0**	**30 days**	**Tue 14-07-01**	**Tue 14-08-05**	
1		**Scope**	**1 day**	**Tue 14-07-01**	**Tue 14-07-01**	
2		Q&A Session	1 day	Tue 14-07-01	Tue 14-07-01	
3		Determine project scope	4 hrs	Tue 14-07-01	Tue 14-07-01	
4		**Analysis/Software Requirements**	**2 days**	**Wed 14-07-02**	**Thu 14-07-03**	
5		Draft preliminary software specifica	2 days	Wed 14-07-02	Thu 14-07-03	3
6		**Design**	**5 days**	**Fri 14-07-04**	**Wed 14-07-09**	
7		Develop functional specifications	1 day	Fri 14-07-04	Fri 14-07-04	
8		Review functional specifications	2 days	Sat 14-07-05	Mon 14-07-07	7
9		Powerpoint Preparation	1 day	Mon 14-07-07	Mon 14-07-07	
10		Presentation	1 day	Wed 14-07-09	Wed 14-07-09	
11		**Development**	**18 days**	**Thu 14-07-10**	**Wed 14-07-30**	
12		Review functional specifications	1 day	Thu 14-07-10	Thu 14-07-10	
13		Identify modular/tiered design para	0.5 days	Fri 14-07-11	Fri 14-07-11	12
14		Assign development staff	1 day	Sat 14-07-12	Sat 14-07-12	13
15		**Coding**	**15 days**	**Mon 14-07-14**	**Wed 14-07-30**	**14**
16		Develop Client Code	14 days	Mon 14-07-14	Tue 14-07-29	
17		Develop Server Code	14 days	Mon 14-07-14	Tue 14-07-29	
18		Developer testing (primary debuggi	1 day	Wed 14-07-30	Wed 14-07-30	16FS-75%
19		**Testing**	**1 day**	**Mon 14-08-04**	**Mon 14-08-04**	
20		Prepare Test Cases and Complete th	0.25 days	Mon 14-08-04	Mon 14-08-04	
21		**Documentation**	**1 day**	**Tue 14-08-05**	**Tue 14-08-05**	
22		Develop user manuals	1 day	Tue 14-08-05	Tue 14-08-05	16FS-50%

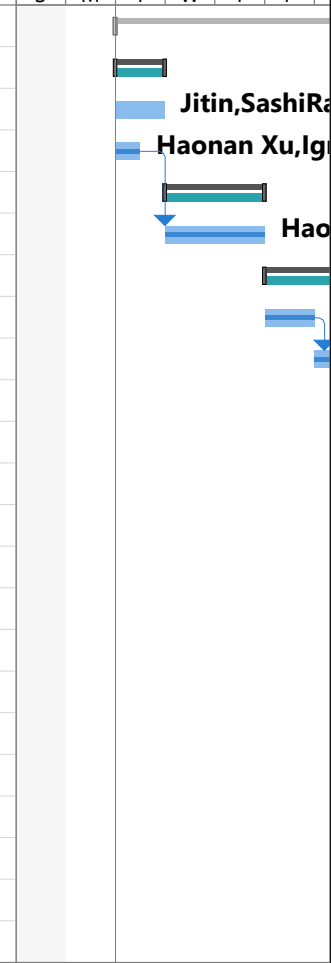

Project: CICS525_ProjectPlanV1
Date: Tue 14-07-08

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

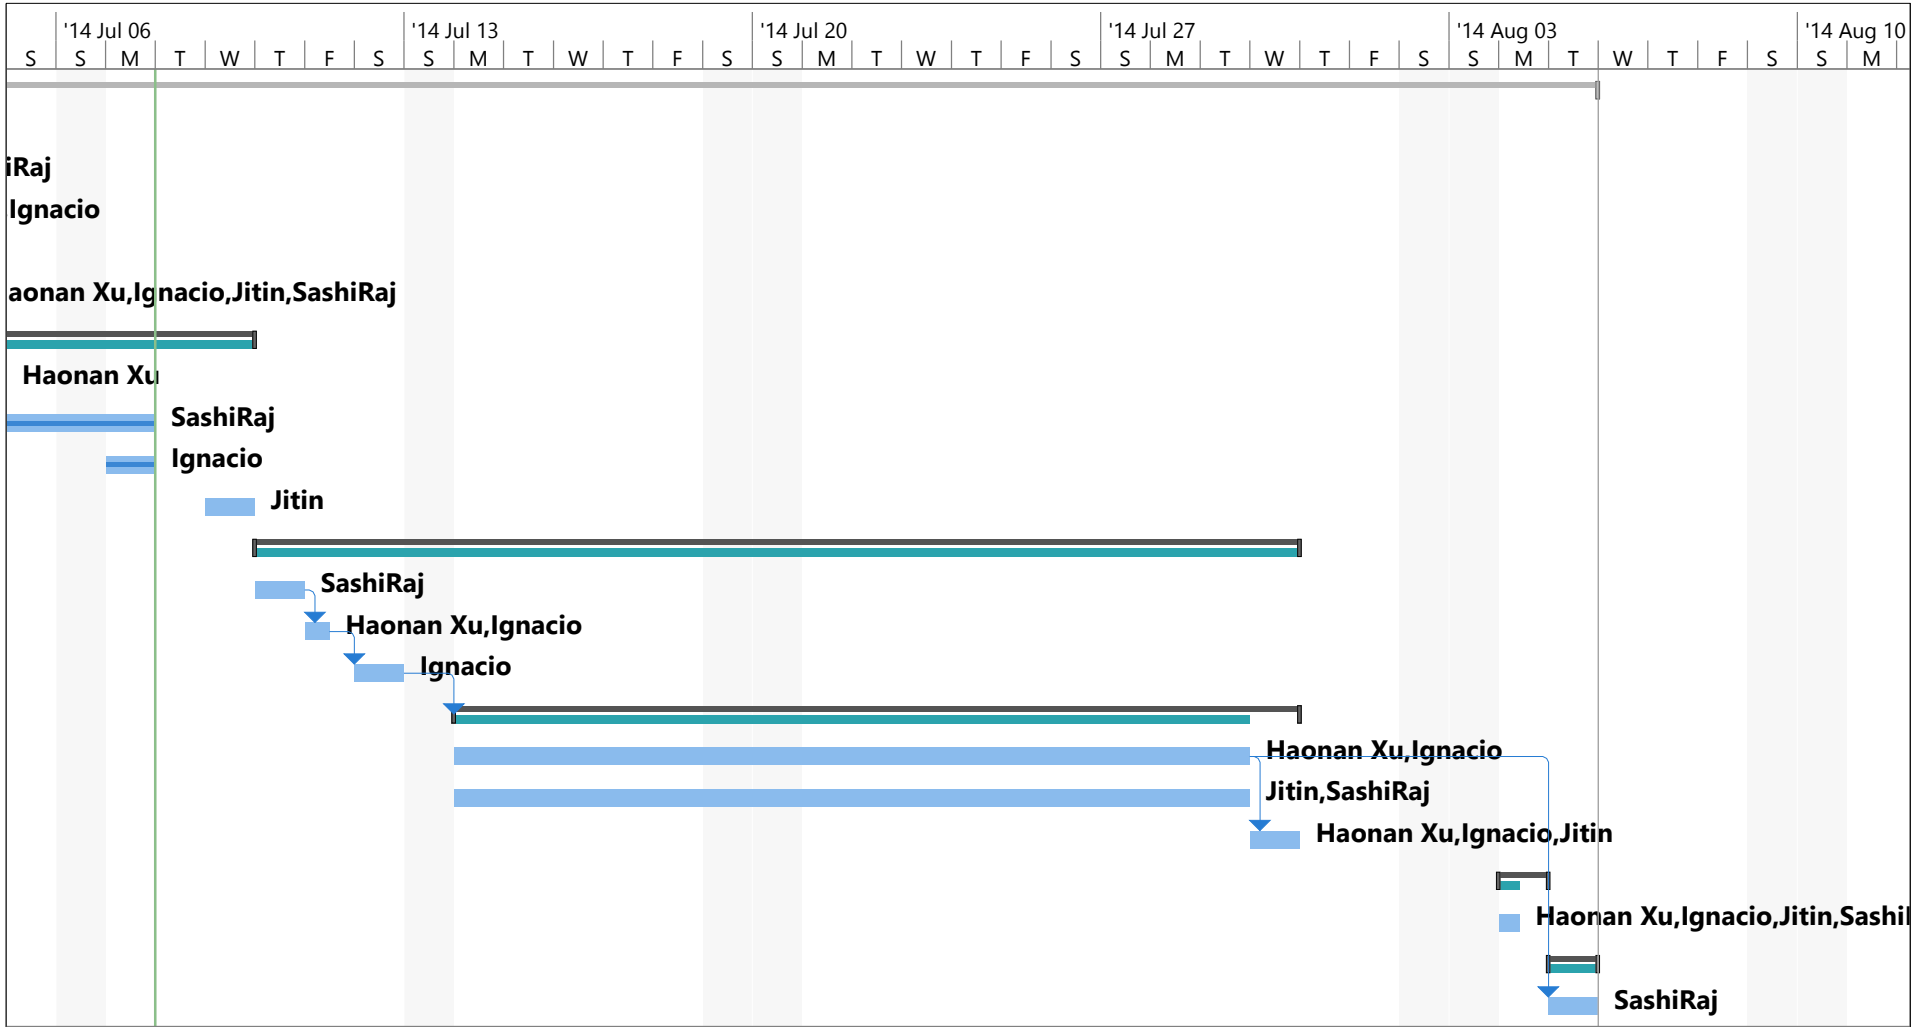

Project: CICS525_ProjectPlanV1
Date: Tue 14-07-08

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
